

Southside Network Authority Regional Connectivity Ring Project Update


Southside Network Authority Board Meeting

August 9, 2024


Outline

- Project Update
- Recruitment Update for SNA Executive Director Position

Permit and Construction Status

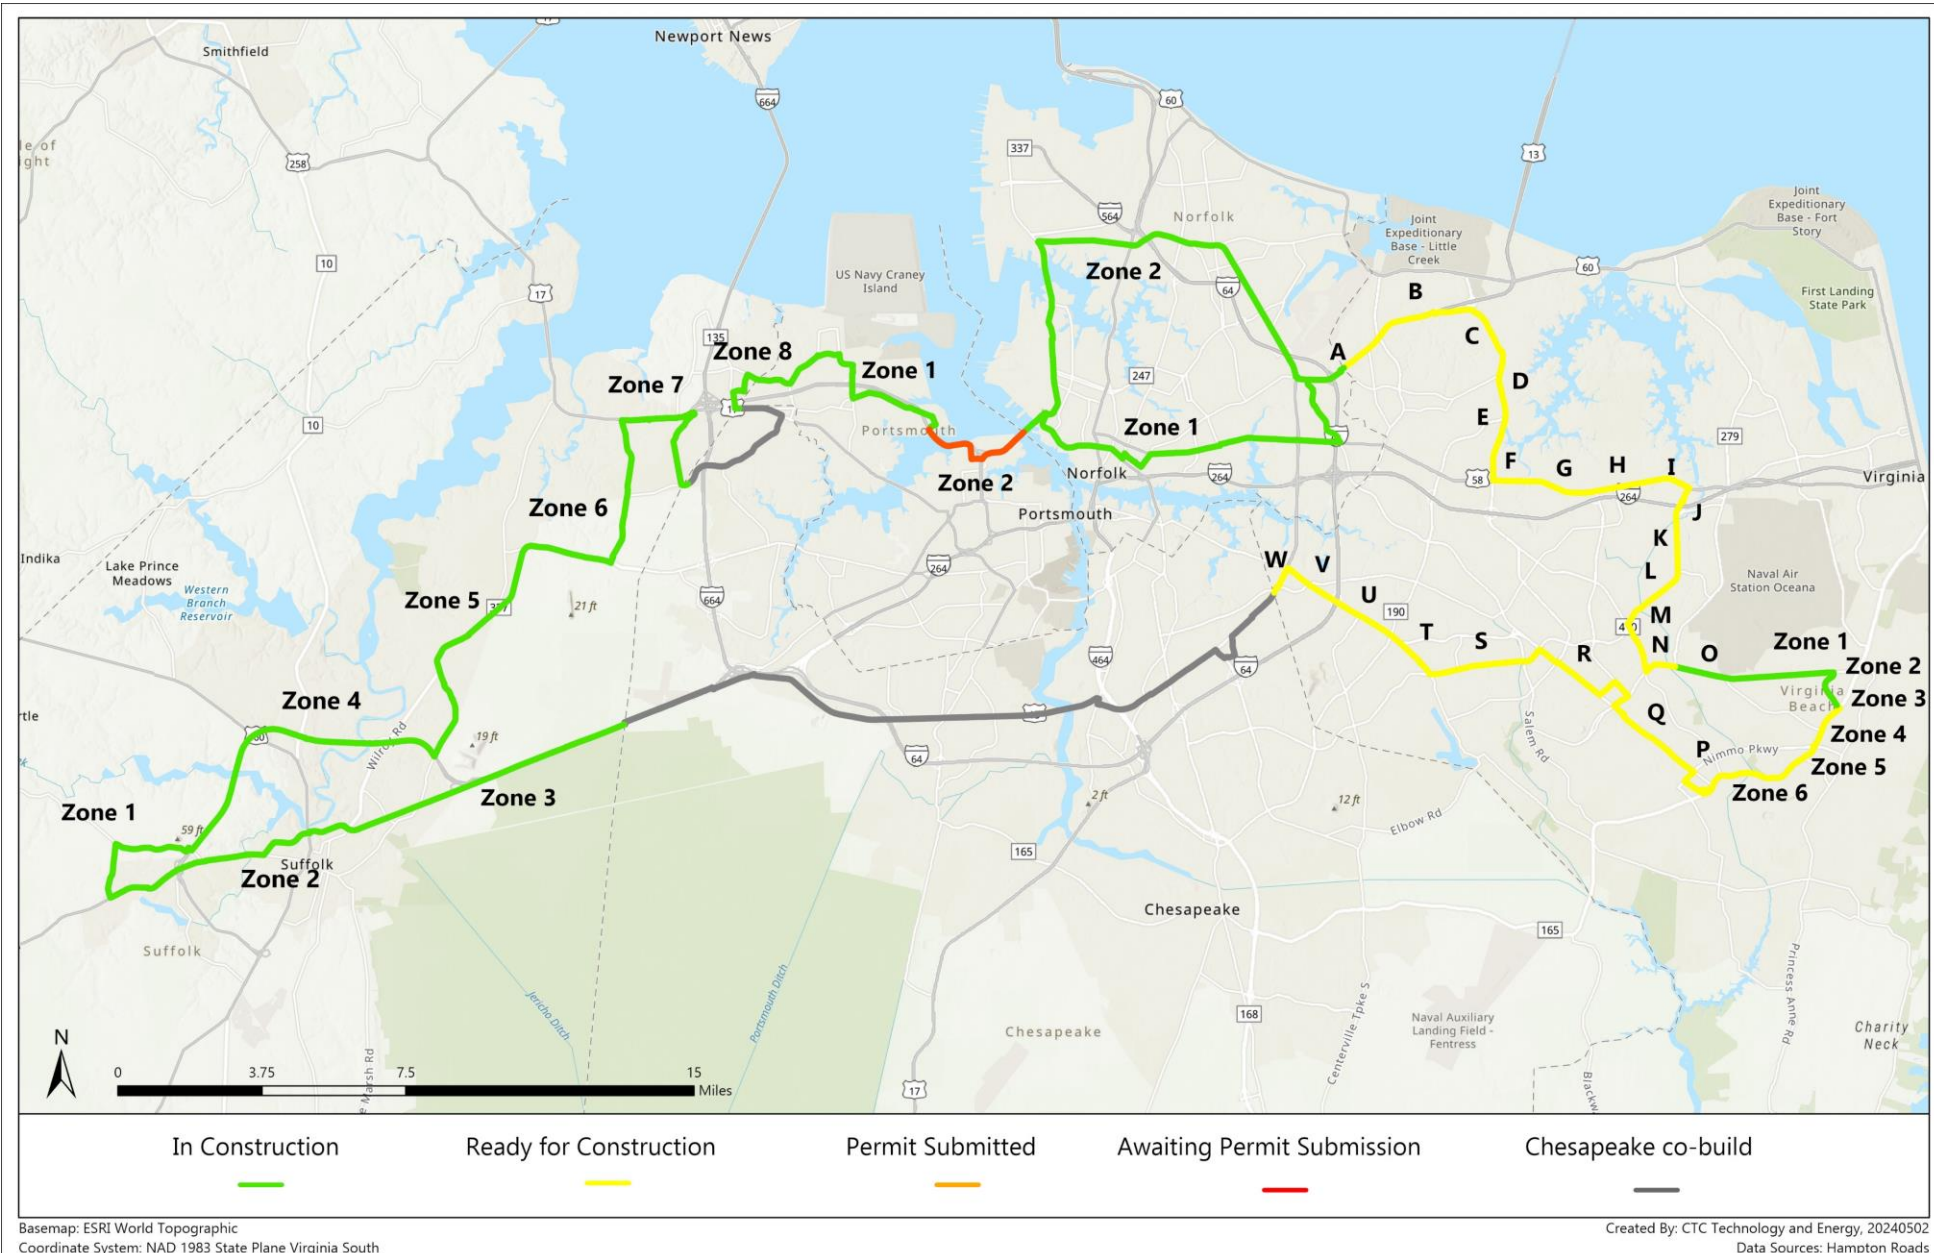

Projected Construction Completion Timeline 2024/25

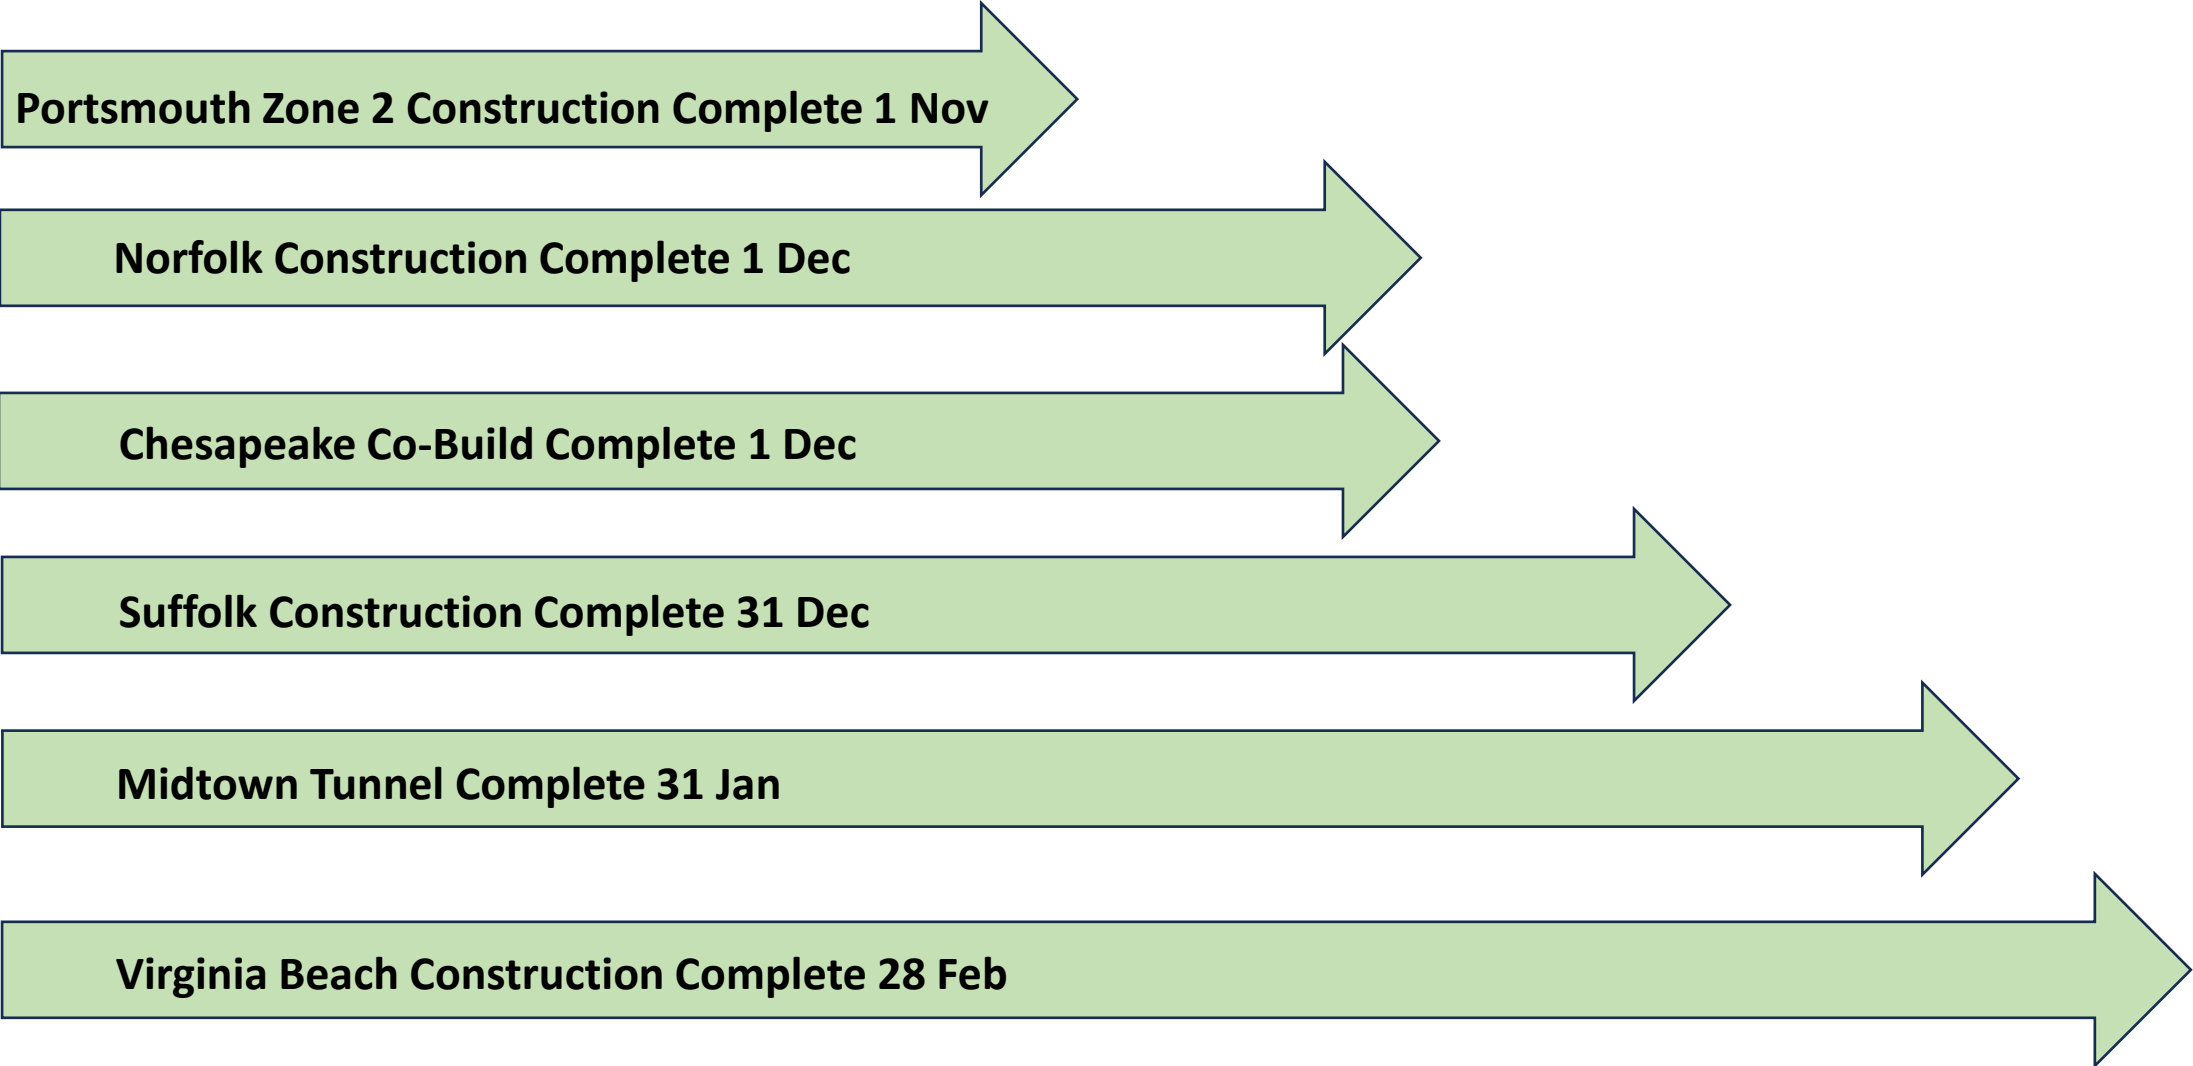

Projected Construction Completion Timeline 2024



Portsmouth – Complete 1 Nov

- Submit W. Freeway Permit to VDOT 8/14
- VDOT Approval 9/4
- Danella 60 days construction

June

July

Aug

Sept

Oct

Nov

Dec 5

Projected Construction Completion Timeline 2024

Norfolk Complete 1 Dec

- Zone 1 Redesign – Brambleton and Courthouse (Permit Approved)
 - Complete design to include 2 HRT Crossings 8/30
 - Design approved by HRT 9/27
 - Danella 60 days construction complete 1 Dec
- Design change E. Little Creek and Tidewater (Bypass Underpass)
 - Submit change to permits 8/30; receive approval 9/6
 - Danella 45 days construction; complete 1 Nov
- 4 Bridge revisions/submittals 8/23
 - Receive Approval 9/13
 - Danella 60 days construction complete 28 Nov

June

July

Aug

Sept

Oct

Nov

Dec 6

Projected Construction Completion Timeline 2024

Chesapeake Co-Build Complete 1 December

- Chesapeake turnover of SNA co-build portion (19 miles) 1 November
 - Gilmerton Bridge completed
 - 4 of 6 remaining railroad permits approved and awaiting flagmen; 2 permit requests in progress
 - Danella 30 days construction to push fiber through conduit

Projected Construction Completion Timeline 2024

Suffolk Complete 31 Dec

- SPSA Flyover
 - Submit Permit 8/28; Approval received 9/11
 - Danella 75 days construction; complete 31 Dec
- Zone 1 (Highway 58 Construction)
 - Danella able to construct all but 1500' near Kenyon and school
 - Danella access to 1500' 1 Dec; 31 Dec complete
- Zones 6/7 (Shoulders Hill, Bridge Rd.)
 - Submit redesign 8/28; Approve by 9/11
 - Danella 60 days construction; complete 11/15
- 4 Railroads
 - Submit permits 8/9; Receive approval and schedule flagmen 9/1; Flagmen available 12/1
 - Danella 30 days construction complete 31 Dec

June

July

Aug

Sept

Oct

Nov

Dec 8

Projected Construction Completion Timeline 2024/5

Midtown Tunnel Complete 31 Jan



- Final design submitted to VDOT 8/30
- Approval SNA and VDOT Agreement 11/1
 - Valuation determined
 - In-kind fiber identified
- Danella 90 days construction

Projected Construction Completion Timeline 2024/25

Virginia Beach Complete 28 Feb 25

- 29 Permits approved
- 2 permits under construction (O, 1)
 - Priority on permits A-L
 - A-L connect GTS Ops Center to Midtown Tunnel
- Danella 180 days construction

Aug

Sept

Oct

Nov

Dec

Jan

Feb 10

SNA Executive Director Recruitment - Timeline

- Job announcement posted July 3, 2024
 - Conduct initial interviews mid-September - virtual
 - Conduct second interviews mid-October – in person
 - Select candidate and negotiate contract – late October
 - SNA Board vote on selectee and contract - November 8 SNA Board Meeting
 - Executive Director conducts turnover with selectee December 2024
- Initial meeting with VRS regarding retirement plan 6 Aug
