


Southside Network Authority
Regional Connectivity Ring
Project Update


Southside Network Authority Board Meeting

September 13, 2024

Permit and Construction Status

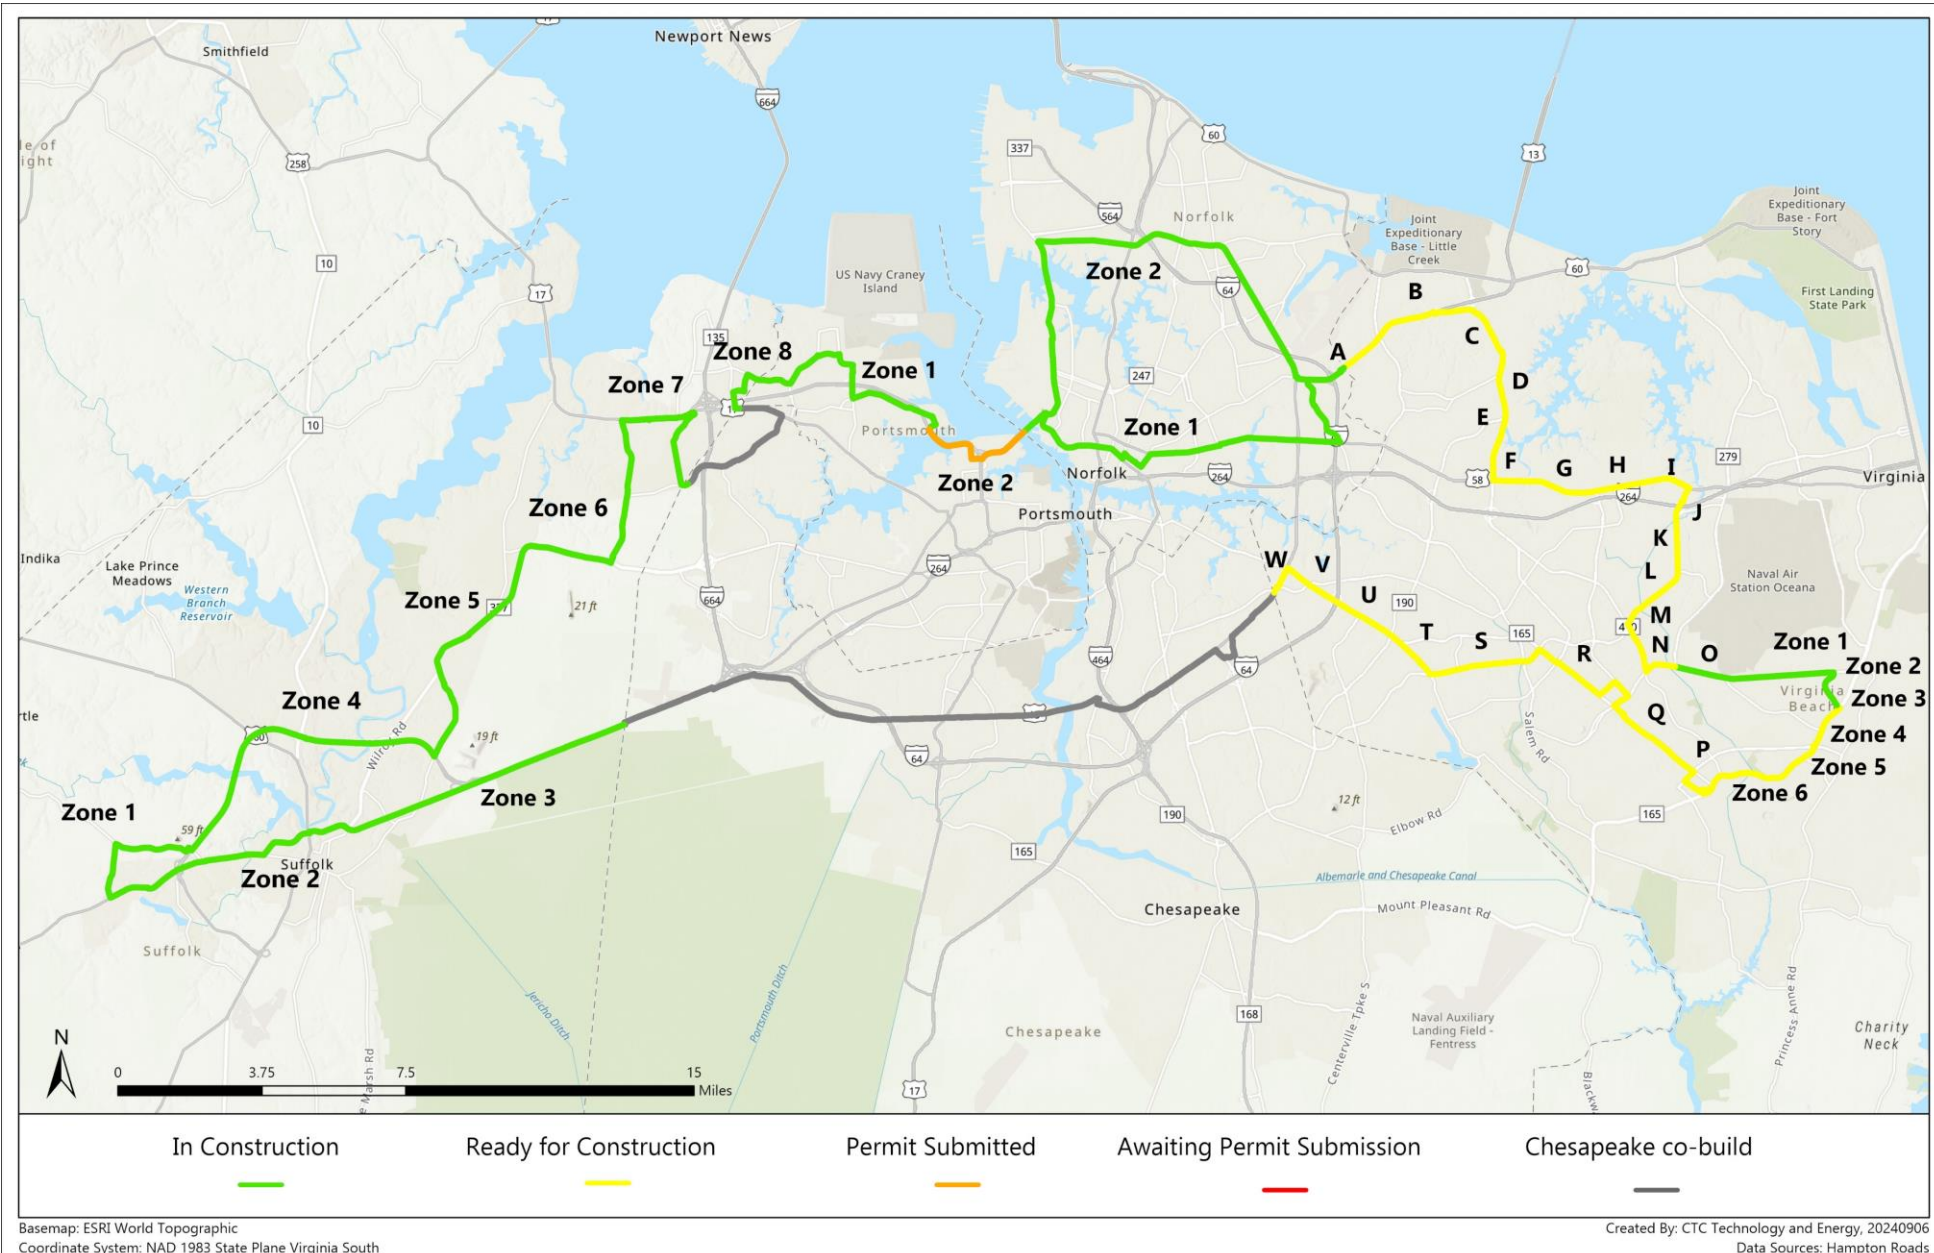

Projected Construction Completion Timeline 2024/25

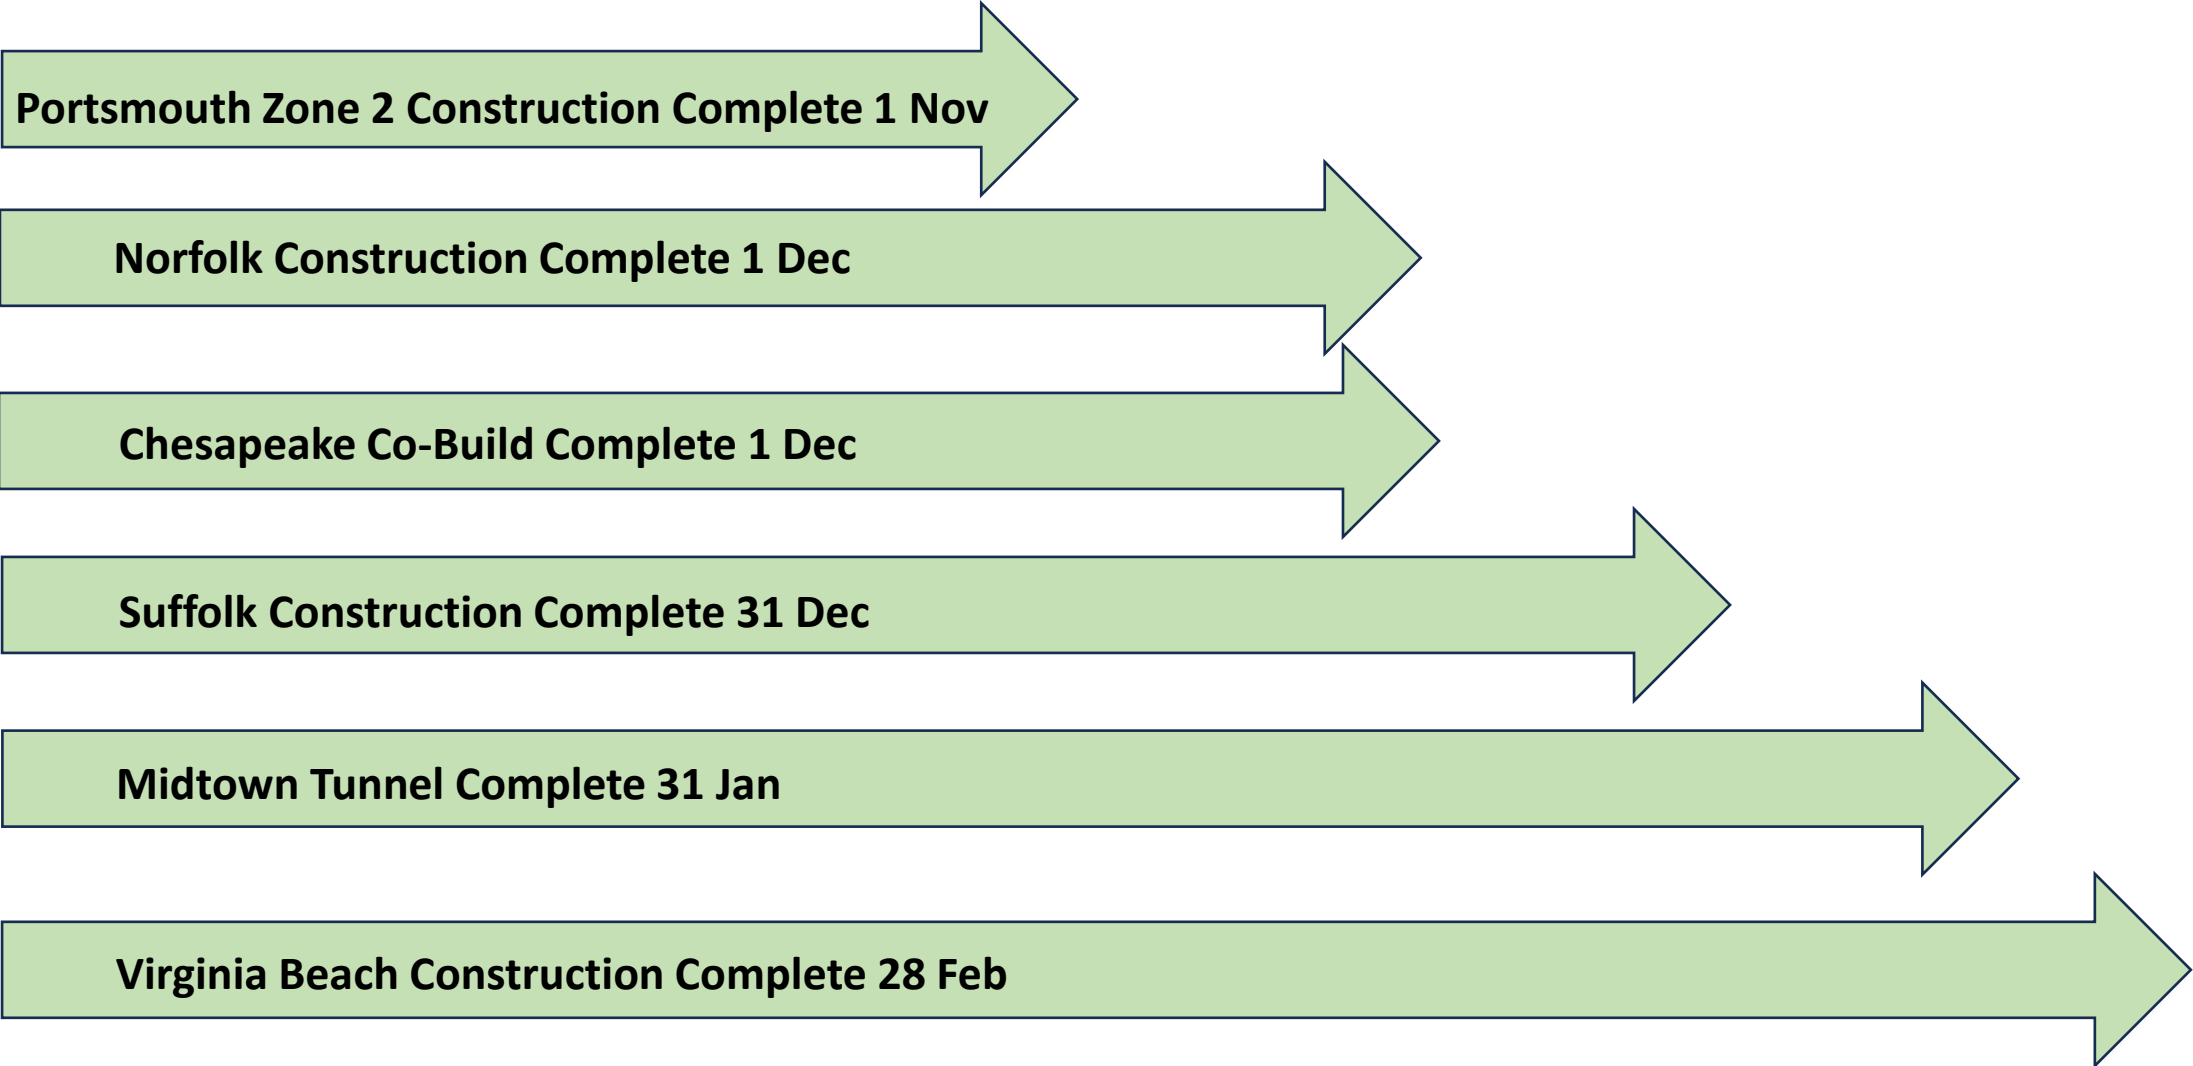

Aug Sept Oct Nov Dec Jan Feb ³

Projected Construction Completion Timeline 2024



Portsmouth – Complete 1 Nov

- Submit W. Freeway Permit to VDOT 8/14 **(Submitted)**
- VDOT Approval **(Expect VDOT approval and Resource Sharing Agreement week of 9/16)**
- Danella 60 days construction

Projected Construction Completion Timeline 2024

Norfolk Complete 1 Dec

- Zone 1 Redesign – Brambleton and Courthouse (Permit Approved)
 - Complete design to include 2 HRT Crossings 8/30 (**CTC submitted permit change 8/30 including 2 HRT crossings**)
 - Design approved by HRT 9/27
 - Danella 60 days construction complete 1 Dec
- Design change E. Little Creek and Tidewater (Bypass Underpass)
 - Submit change to permits 8/30 (**CTC submitted permit change 8/30**); receive approval 9/13
 - Danella 45 days construction; complete 1 Nov
- 4 Bridge revisions/submittals 8/23 (**Revisions submitted**)
 - Receive Approval 9/13 (**Approved 9/6**)
 - Danella 60 days construction complete 28 Nov
- 5 RRs; **2 completed; 3 awaiting flagmen**

June

July

Aug

Sept

Oct

Nov

Dec 5

Projected Construction Completion Timeline 2024

Chesapeake Co-Build Complete 1 December

- Chesapeake turnover of SNA co-build portion (19 miles)
1 November
 - Gilmerton Bridge completed
 - 4 of 6 remaining railroad permits approved and awaiting flagmen; 2 permit requests in progress
 - Danella 30 days construction to push fiber through conduit

Projected Construction Completion Timeline 2024

Suffolk Complete 31 Dec

- SPSA Flyover
 - Submit Permit 8/28; Approval received 9/13 CTC meeting (**Permit revision submitted 8/30**)
 - Danella 75 (**90**) days construction; complete 31 Dec
- Zone 1 (Highway 58 Construction)
 - Danella able to construct all but 1500' near Kenyon and school, **Danella begins construction 9/9**
 - Danella access to 1500' 1 Dec; 31 Dec complete
- Zones 6/7 (Shoulders Hill, Bridge Rd.)
 - Submit redesign 8/28; Approve by 9/13 (**CTC submitted revised permit 8/30**)
 - Danella 60 days construction; complete 11/15
- 10 Railroads/Overpasses
 - **5 approved [NSR (2) and CSX (3)]; 5 submitted for final approval (G&W); Flagmen available approximately 12/6**
 - Danella 30 days construction complete 31 Dec

June

July

Aug

Sept

Oct

Nov

Dec 7

Projected Construction Completion Timeline 2024/25

Midtown Tunnel Complete 31 Jan

- Final design (submitted; VDOT conducting final review and Resource Sharing Agreement week of 9/16)
- SNA Team working with VDOT Regional Administrator's Staff
- Approval SNA and VDOT Agreement 11/1
- Danella 90 days construction

July

Aug

Sept

Oct

Nov

Dec

Jan 8

Projected Construction Completion Timeline 2024/25

Virginia Beach Complete 28 Feb 25

- 29 Permits approved
- **SNA letter to CTC and Danella directing “way-ahead”**
 - 2 permits under construction (O, 1)
 - **Danella to begin construction immediately on permits A, B, C, E, F, H, I, J, K, N, P, Q, T, U, V, W, 2, 3, 4, 5, and 6**
 - **CTC to revise permits D, L, M, N, R, and S**
 - **180 days construction**
