

# I-564 Intermodal Connector (Project in Financial Closeout)

UPC # 18968

## OVERVIEW

**Description:** Construct Intermodal Connector from I-564 to the Norfolk Naval Base/Norfolk International Terminal.

**Street (Route):** I-564

**From:** I-564

**To:** Norfolk Naval Base/Norfolk International Terminal

**Length (mi):** 1.6

**Jurisdiction/Agency:** Norfolk

**System:** Interstate

**Scope:** New Construction


**Oversight:** Federal Oversight

**Administered By:** VDOT

**Regionally Significant for Air Quality:** Yes

**CMAQ:** No

**RSTP:** No

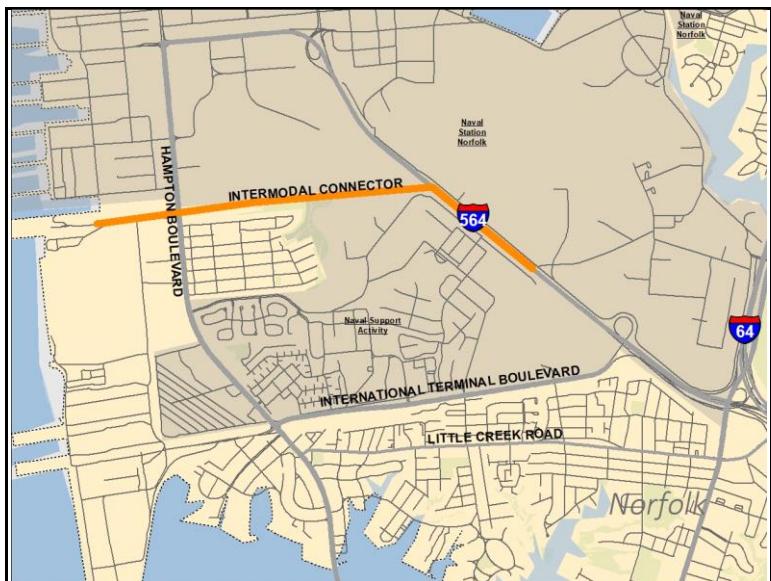

## HRTPO Notes

## SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
Preliminary Engineering	7/1/1998	4/24/2001	Complete
Right of Way	4/24/2001	3/16/2015	Complete
Construction	3/16/2015	3/15/2019	Complete

## COSTS AND EXPENDITURES

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>
Preliminary Engineering	\$10,995,515	\$10,938,255	99%
Right of Way	\$25,964,832	\$26,042,133	100%
Construction	\$0	\$0	-
<b>TOTAL</b>	<b>\$36,960,347</b>	<b>\$36,980,388</b>	<b>100%</b>

### *Recent Expenditures*

<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
	<i>3</i>	<i>2</i>	<i>1</i>
\$77,008	\$16,536	\$11,910	\$1,672
\$109,234	\$15,229	\$4,761	-
\$0	-	-	-

# I-564 Intermodal Connector (Project in Financial Closeout)

UPC # 18968

## ALLOCATIONS

Fund Source(s)	Previous	FY 2024	FY 2025	FY 2026	FY 2027	<b>TOTAL</b>
TBD	\$1,949,070	\$0	\$0	\$0	\$0	\$1,949,070
STM	\$1,291,302	\$0	\$0	\$0	\$0	\$1,291,302
STF	\$7,401,888	\$0	\$0	\$0	\$0	\$7,401,888
NHS	\$10,203,486	\$0	\$0	\$0	\$0	\$10,203,486
FRAN	\$3,404,000	\$0	\$0	\$0	\$0	\$3,404,000
DEMO	\$16,137,144	\$0	\$0	\$0	\$0	\$16,137,144
CPR	\$1,425	\$0	\$0	\$0	\$0	\$1,425
BOM	\$2,652,227	\$0	\$0	\$0	\$0	\$2,652,227
<b>TOTAL</b>	<b>\$43,040,542</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$43,040,542</b>

## SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
