

Clearfield Avenue (Cleveland Street to Virginia Beach Boulevard)

UPC # 123178

OVERVIEW

Description: Construct 0.26 miles of 2-way left-turn lanes and 1,320' of 5-foot sidewalk on Clearfield Ave to Virginia Beach Blvd. Traffic signal at Clearfield Ave/Virginia Beach Blvd to be modified by relocating signal in the southwest quadrant.

Street (Route): Clearfield Avenue

From: Cleveland Street

To: Virginia Beach Boulevard

Length (mi): 0.312

Jurisdiction/Agency: Virginia Beach

System: Urban

Scope: Reconstruction w/ Added Capacity

Oversight: Non-Federal Oversight

Administered By: Locality


Regionally Significant: No

CMAQ: No

RSTP: No

TAP: No

CRP: No

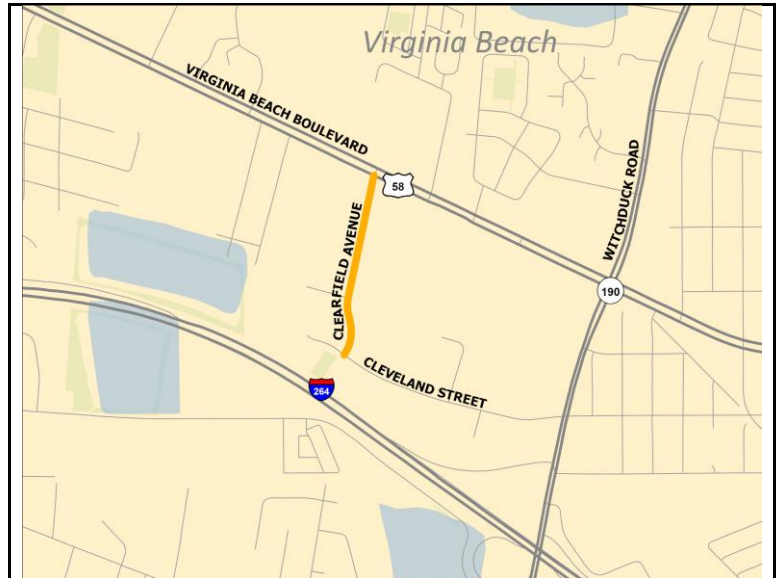

HRTPO Notes

Revised 7/31/2025: Amendment to add project to the TIP.

SCHEDULE

	Start	End	Status
Preliminary Engineering	12/26/2025	2/18/2028	FFY 2026
Right of Way	2/18/2028	11/10/2028	FFY 2028
Construction	11/10/2028	10/29/2029	FFY 2029

COSTS AND EXPENDITURES

	Cost Estimates	Total Expenditures	Percent Expended
Preliminary Engineering	\$860,726	\$0	0%
Right of Way	\$8,221,175	\$0	0%
Construction	\$5,964,378	\$0	0%
TOTAL	\$15,046,279	\$0	0%

Recent Expenditures

Latest Quarter	Previous 3 Quarters		
	3	2	1
	-	-	-
	-	-	-
	-	-	-

Clearfield Avenue (Cleveland Street to Virginia Beach Boulevard)
UPC # 123178

ALLOCATIONS

Fund Source(s)	Previous	FY 2024	FY 2025	FY 2026	FY 2027	TOTAL
DGP/State	\$0	\$0	\$0	\$900,000	\$2,556,539	\$3,456,539
TOTAL	\$0	\$0	\$0	\$900,000	\$2,556,539	\$3,456,539

SCHEDULED OBLIGATIONS

Phase	Fund Source	Previous	FY 2024	FY 2025	FY 2026	FY 2027	Match
PE	Other				\$860,726		
	Subtotal				\$860,726		
	TOTAL				\$860,726		

Source of Project Data: Virginia Department of Transportation.
