

Atkinson Boulevard Construction (Project in Financial Closeout)

UPC # 4483

OVERVIEW

Description: Construct a 4 lane roadway from Warwick Blvd (Rte 60) to Jefferson Ave (Rte 143).

Street (Route): Atkinson Boulevard

From: Warwick Boulevard (Route 60)

To: Jefferson Avenue (Route 143)

Length (mi): 1.2

Jurisdiction/Agency: Newport News

System: Urban

Scope: New Construction


Oversight: Non-Federal Oversight

Administered By: Locality

Regionally Significant for Air Quality: Yes

CMAQ: No

RSTP: Yes

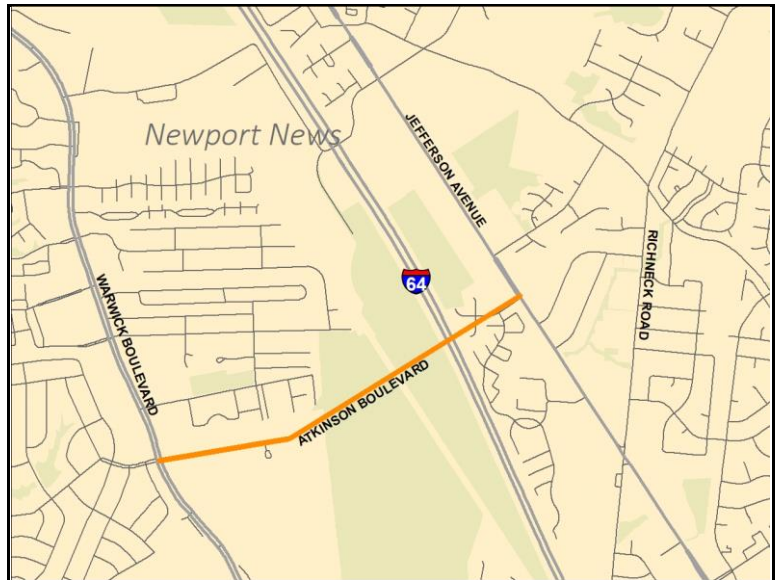

HRTPO Notes

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	6/8/1987	9/14/2016	Complete
<i>Right of Way</i>	9/14/2016	5/11/2017	Complete
<i>Construction</i>	5/11/2017	9/1/2020	Complete

COSTS AND EXPENDITURES

	<i>Recent Expenditures</i>		
	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>
<i>Preliminary Engineering</i>	\$5,692,574	\$5,692,574	100%
<i>Right of Way</i>	\$1,389,174	\$694,587	50%
<i>Construction</i>	\$60,537,493	\$56,231,904	93%
TOTAL	\$67,619,241	\$62,619,065	93%

<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
	<i>3</i>	<i>2</i>	<i>1</i>
\$0	-	-	-
\$0	-	-	-
\$121,228	\$591,749	\$2,028,653	\$6,049,347

Atkinson Boulevard Construction (Project in Financial Closeout)

UPC # 4483

ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>TOTAL</i>
STP	\$1,305,610	\$0	\$0	\$0	\$0	\$1,305,610
STM	\$9,632,321	\$0	\$0	\$0	\$0	\$9,632,321
STF	\$7,195,116	\$0	\$0	\$0	\$0	\$7,195,116
RSTP	\$40,529,277	\$0	\$0	\$0	\$0	\$40,529,277
RS	\$9,500,000	\$0	\$0	\$0	\$0	\$9,500,000
LOM	\$20,408	\$0	\$0	\$0	\$0	\$20,408
LOC	\$62	\$0	\$0	\$0	\$0	\$62
BOM	\$200,000	\$0	\$0	\$0	\$0	\$200,000
TOTAL	\$68,382,794	\$0	\$0	\$0	\$0	\$68,382,794

SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
