

I-64 Peninsula Widening - Segment 3 (Project in Financial Closeout)

UPC # 106689

OVERVIEW

Description: Extend the 3 lane section of I-64 from Rt 199 East of Williamsburg (Exit 242) to Rt 199 West of Williamsburg (Exit 234). Work to include one additional EB and WB 12' wide travel lane and 12' wide shoulder lane within the existing median space.

Street (Route): I-64

From: Route 199 east of Williamsburg (Exit 242)

To: Route 199 west of Williamsburg (Exit 234)

Length (mi): 8.36

Jurisdiction/Agency: Multit-Jurisdictional

System: Interstate

Scope: Reconstruction w/ Added Capacity


Oversight: Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: Yes

CMAQ: No

RSTP: No

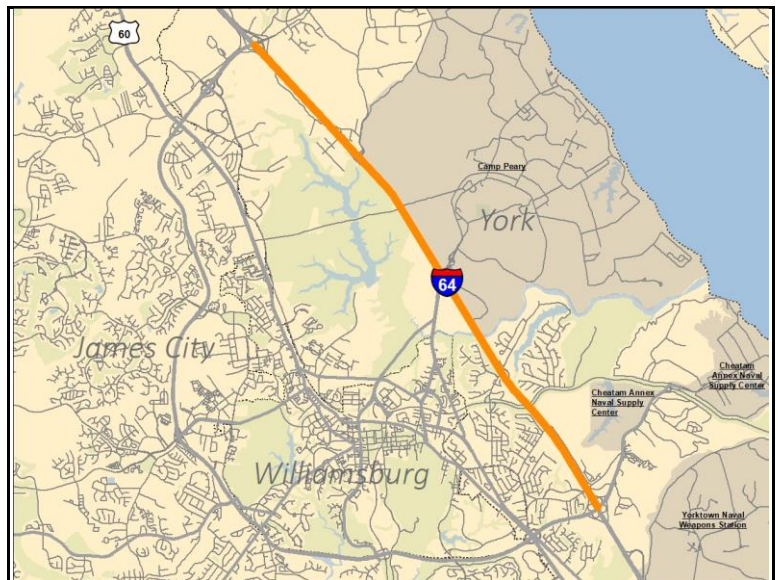

HRTPO Notes

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
Preliminary Engineering	3/1/2016	9/7/2017	Complete
Right of Way	9/7/2017	10/10/2017	Complete
Construction	10/10/2017	12/6/2021	Complete

COSTS AND EXPENDITURES

	Recent Expenditures			Previous 3 Quarters			
	Cost Estimates	Total Expenditures	Percent Expended	Latest Quarter	3	2	1
Preliminary Engineering	\$10,000,000	\$5,763,189	58%	\$141,867	\$28,074	\$64,848	\$26,676
Right of Way	\$0	\$0	-	\$0	-	-	-
Construction	\$112,893,996	\$88,907,818	79%	\$39,529,670	\$13,467,800	\$16,717,193	\$9,222,751
TOTAL	\$122,893,996	\$94,671,007	77%				

I-64 Peninsula Widening - Segment 3 (Project in Financial Closeout)
UPC # 106689

ALLOCATIONS

Fund Source(s)	Previous	FY 2024	FY 2025	FY 2026	FY 2027	TOTAL
HRTAC	\$122,893,996	\$0	\$0	\$0	\$0	\$122,893,996
TOTAL	\$122,893,996	\$0	\$0	\$0	\$0	\$122,893,996

SCHEDULED OBLIGATIONS

Phase	Fund Source	Previous	FY 2024	FY 2025	FY 2026	FY 2027	Match
CN	Other	\$109,577,147	\$3,316,849				
	Subtotal	\$109,577,147	\$3,316,849				
	TOTAL	\$109,577,147	\$3,316,849				

Source of Project Data: Virginia Department of Transportation.
