

Southside Network Authority (SNA)  
Board Meeting  
June 11, 2021

Regional Connectivity Ring  
Contract Negotiations/Near Term Actions

Steven DeBerry  
Executive Director, SNA


# Agenda

- Review current status of near-term efforts
- Proposed change in the timeline for Construction and Maintenance Invitation to Bid (IFB) and the addition of an accompanying Financing Request for Procurement (RFP)
- Approve changes to the adopted Fiscal Year (FY) 2022 Budget
- Next Steps

# Projected Timeline for Near-Term Efforts

- Construction and Maintenance Pre-qualification RFP – Review Committee is currently evaluating the 9 responses received
- Municipal Financial Advisor RFP – Review Committee is currently evaluating the 3 responses received
- P3 RFP – Issued May 20, 2021 (responses due August 24, 2021)
- Construction and Maintenance IFB and Financing RFP – Propose Issue July 8, 2021 instead of currently scheduled August 5, 2021 (responses would be due August 24, 2021 vs September 14, 2021)

# Relative Timeline Comparison for RCR Strategies

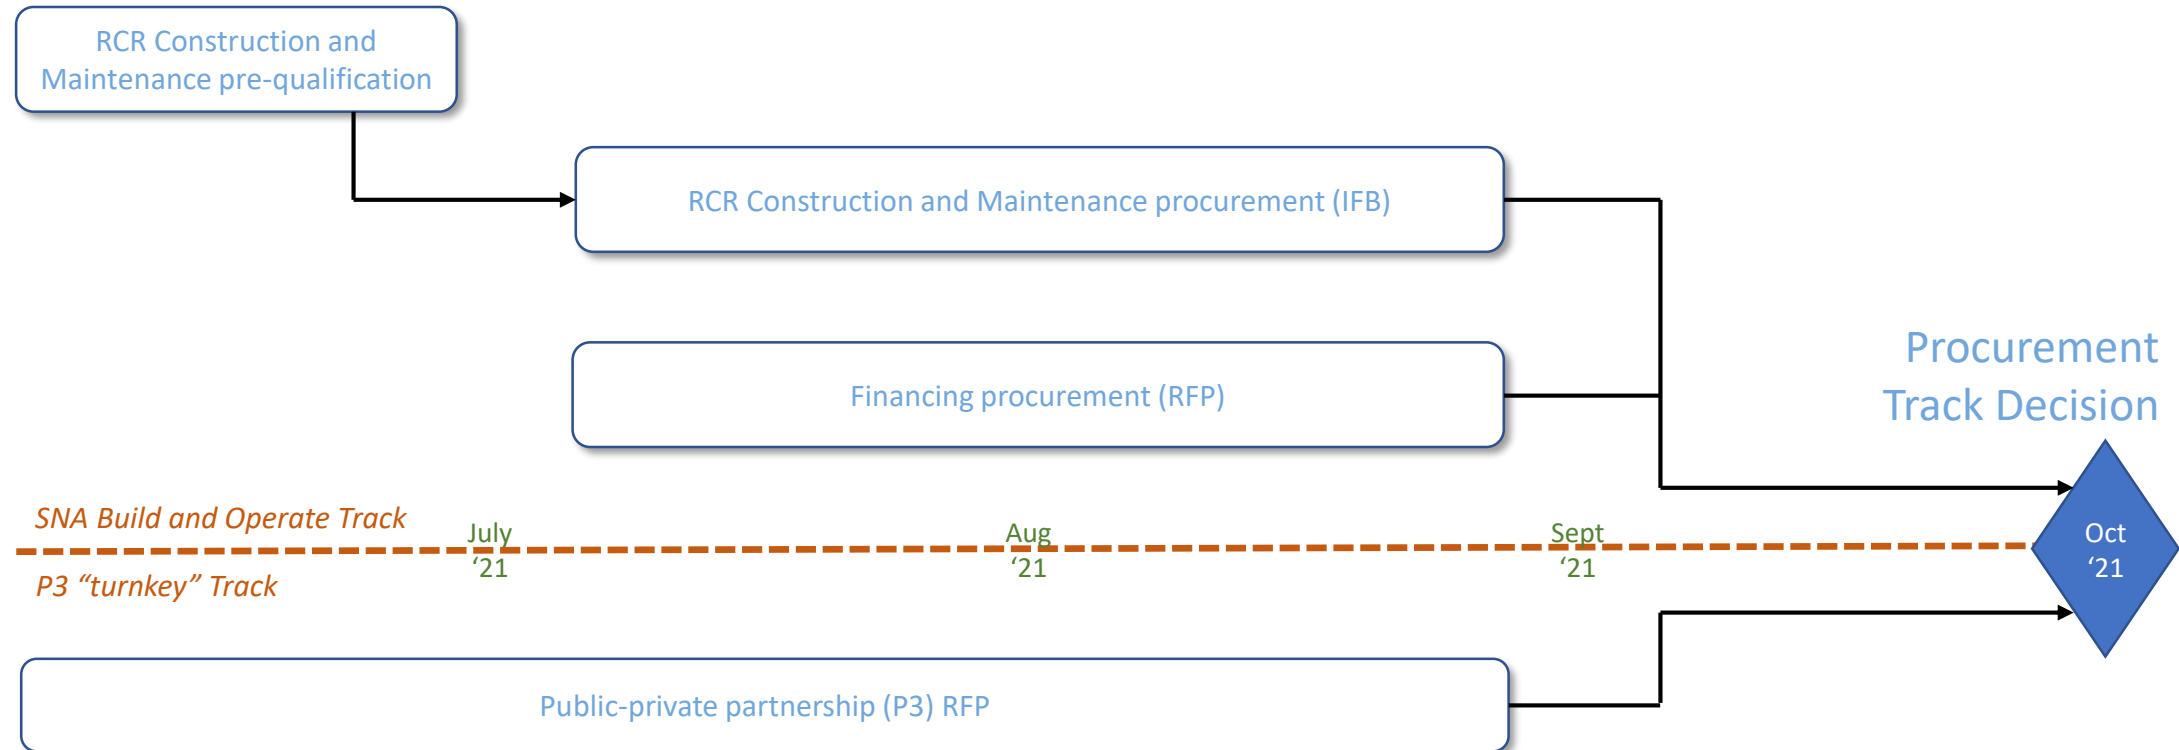

# Next Steps

- Execute procurement strategy per Board direction
- Prioritize and align remaining contract and governance items
- Continue to pursue potential grants and strategic partnerships
- Work with 5 Southside cities regarding American Rescue Plan and American Jobs Plan as funding mitigation strategy for building the Regional Connectivity Ring
